



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,
M/S Pelican Builders & Property Consultant (Pvt) Ltd.

Reference # CED/TFL **4495** (Dr. Ali Ahmed)

Dated: 15-01-2024

Reference of the request letter # PB/DHAb22/DHA/MALL/184

Dated: 11-01-2024

Tension Test Report (Page -1/1)

Date of Test 16-01-2024

Gauge length 8 inches

Description Deformed Steel Bar Tensile and Bend Test as per ASTM-A615

Sr. No.	Weight (lbs/ft)	Diameter/ Size		Area (in ²)		Yield load (kg)	Breaking Load (kg)	Yield Stress (psi)		Ultimate Stress (psi)		Elongation (inch)	% Elongation	Remarks
		Nominal (#)	Actual (inch)	Nominal	Actual			Nominal	Actual	Nominal	Actual			
1	0.364	3	0.369	0.11	0.107	3500	4800	70200	72180	96200	99000	1.00	12.5	
2	0.365	3	0.369	0.11	0.107	3600	4800	72200	74050	96200	98800	1.00	12.5	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Note: only two samples for tensile and one sample for bend test														
Bend Test														
#3 Bar Bend Test Through 180° is Satisfactory														

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
- 2- The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,

Resident Engineer
NESPAK

Development of a Controlled Access Corridor Facility from Niazi Interchange to Babu Sabu Interchange, Lahore, Package – II (km 3+650 to km 7+300)
(WMI 7009)

Reference # CED/TFL **4496** (Dr. Ali Ahmed)

Dated: 15-01-2024

Reference of the request letter # 3772/103/NBI(P-II)/MWA/04/183 Dated: 01-01-2024

Tension Test Report (Page – 1/2)

Date of Test 16-01-2024

Gauge length 640 mm

Description Steel Strand Tensile Test as per ASTM A-416-94a

Sr. No.	Nominal Diameter	Nominal Weight	Measured weight	Yield strength clause (6.3)		Breaking strength clause (6.2)		Young's Modulus of Elasticity	% Elongation	Remarks / Coil No.
	(mm)	(kg/km)	(kg/km)	(kg)	(kN)	(kg)	(kN)	E, GPa		
1	15.24 (0.6")	1102.0	1108.0	24500	240.35	27300	267.81	198	>3.50	7075
-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	
Only one sample for Test										

Witness by M Saleem (M.S NESPAK)

Note:

1. Modulus of Elasticity is based on nominal steel area of the steel strand vide clause 13.3 of ASTM – A416a
2. Load versus percentage strain graphs are attached

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
2. The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,

Resident Engineer
NESPAK


Development of a Controlled Access Corridor Facility from Niazi Interchange to Babu Sabu Interchange, Lahore, Package – II (km 3+650 to km 7+300)
(WMI 7009)

Reference # CED/TFL **4496** (Dr. Ali Ahmed)

Dated: 15-01-2024

Reference of the request letter # 3772/103/NBI(P-II)/MWA/04/183 Dated: 01-01-2024

Graph (Page – 2/2)

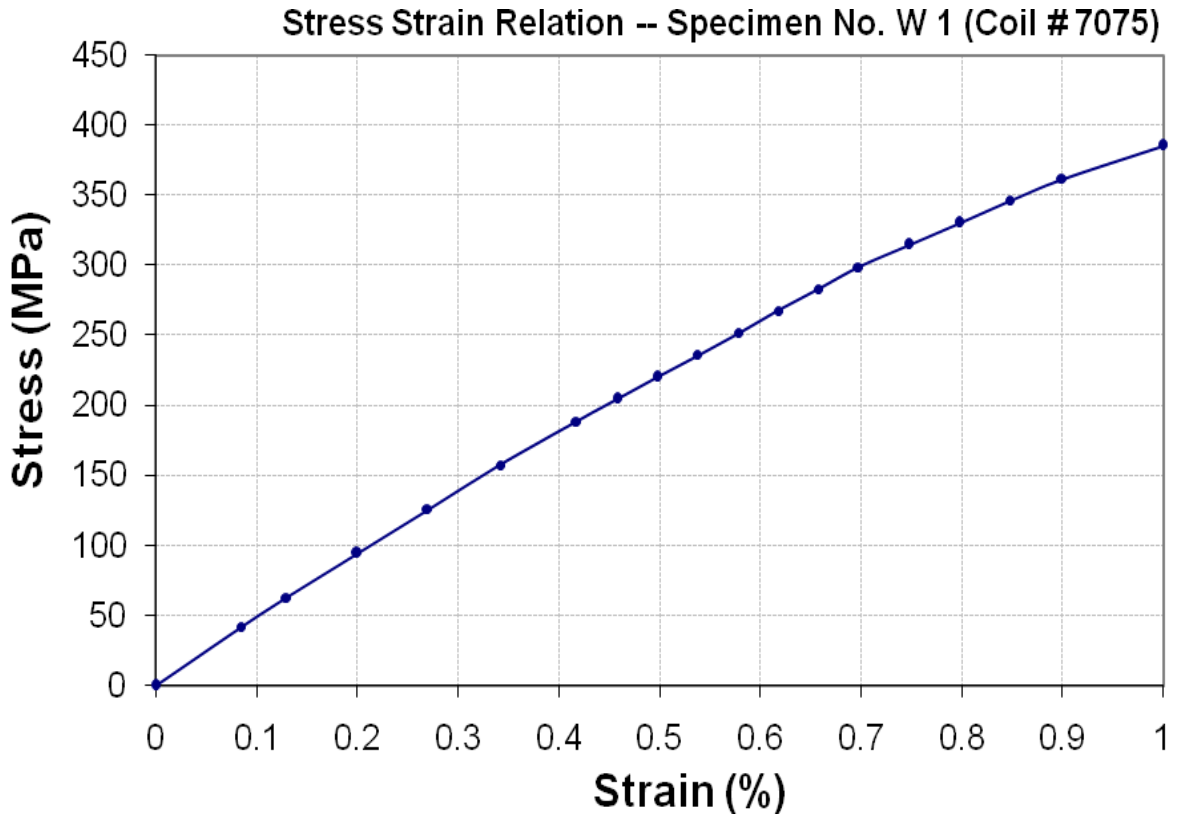

I/C Testing Laboratories
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
- 2- The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,
M/S Engineering Associated Precast (Pvt) Ltd.
Lahore

Reference # CED/TFL **4498** (Dr. Ali Ahmed)
Reference of the request letter # EAP/UET/2024/2674

Dated: 15-01-2024
Dated: 15-01-2024

Tension Test Report (Page -1/2)

Date of Test 16-01-2024
Gauge length 8 inches
Description MS Wire Tensile Test

Sr. No.	Weight (kg/m)	Diameter/ size		Area (mm ²)		Yield load (kg)	Breaking Load (kg)	Yield Stress (MPa) Actual	Ultimate Stress (MPa) Actual	Elongation (inch)	% Elongation	Remarks
		Nominal (mm)	Actual (mm)	Nominal	Actual							
1	0.151	5	4.95	-----	19.3	-----	1240	-----	631	0.40	5.0	
-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	
Note: only one sample for tensile test												
Bend Test												

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
2. The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,
M/S Engineering Associated Precast (Pvt) Ltd.
Lahore

Reference # CED/TFL **4498** (Dr. Ali Ahmed)
Reference of the request letter # EAP/UET/2024/2674

Dated: 15-01-2024
Dated: 15-01-2024

Tension Test Report (Page -2/2)

Date of Test 16-01-2025
Gauge length 640 mm
Description Steel Strand Tensile Test as per ASTM A-416-94a

Sr. No.	Nominal Diameter	Nominal Weight	Measured weight	Yield strength clause (6.3)		Breaking strength clause (6.2)		% Elongation	Remarks/ Coil No.
	(mm)	(kg/km)	(kg/km)	(kg)	(kN)	(kg)	(kN)		
1	9.53 (3/8")	432.0	443.0	8600	84.37	10200	100.06	>3.50	xx
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
Only one sample for Test									

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
- 2- The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,

Assistant Executive Engineer-I
 Central Civil Division No.1
 Pak PWD, Lahore
 (Repair / Replacement of Old Overhead Water Tank (20000 Gallon Capacity) at NSPP
 Lahore.

Reference # CED/TFL **4499** (Dr. Ali Ahmed)
 Reference of the request letter # AEE-I/CCD-I/LHR/167

Dated: 15-01-2024
 Dated: 01-01-2024

Tension Test Report (Page -1/1)

Date of Test 16-01-2024
 Gauge length 8 inches
 Description Deformed Steel Bar Tensile and Bend Test as per ASTM-A615

Sr. No.	Weight	Diameter/ Size (inch)		Area (in ²)		Yield load	Breaking Load	Yield Stress (psi)		Ultimate Stress (psi)		Elongation	% Elongation	Remarks
	(lbs/ft)	Nominal	Actual	Nominal	Actual	(kg)	(kg)	Nominal	Actual	Nominal	Actual	(inch)		
1	0.364	3/8	0.369	0.11	0.107	4200	5100	84200	86520	102200	105100	1.30	16.3	
2	0.388	3/8	0.381	0.11	0.114	4200	5100	84200	81240	102200	98700	1.00	12.5	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Note: only two samples for tensile and one sample for bend test														
Bend Test														
3/8" Dia Bar Bend Test Through 180° is Satisfactory														

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
- 2- The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample /Signed Samples



STRUCTURAL ENGINEERING DIVISION
Test Floor Laboratory
Department of Civil Engineering
University of Engineering and Technology Lahore, 54890
Pakistan. Ph: 92-42-99029202

To,

M/S The Driller Engineers & Contractors
Lahore
(Grand Orchard, DHA-1, Islamabad.)

Reference # CED/TFL **4503** (Dr. Ali Ahmed)
Reference of the request letter # TD/CAL/UET-1024

Dated: 16-01-2024
Dated: 15-01-2024

Tension Test Report (Page – 1/1)

Date of Test 16-01-2024
Gauge length 640 mm
Description Steel Strand Tensile Test as per ASTM A-416-94a

Sr. No.	Nominal Diameter	Nominal Weight	Measured weight	Yield strength clause (6.3)		Breaking strength clause (6.2)		% Elongation	Remarks/ Coil No.
	(mm)	(kg/km)	(kg/km)	(kg)	(kN)	(kg)	(kN)		
1	15.24 (0.6")	1102.0	1116.0	24200	237.40	28800	282.53	>3.50	xx
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	
-	-	-	-	-	-	-	-	-	

Only one sample for Test

I/C Testing Laboratoires
UET Lahore, Pakistan.

Note:

- 1- You can See your reports On Internet in the following web site
http://www.uet.edu.pk/faculties/facultiesinfo/civil/index.html?RID=testing_reports
- 2- The above results pertain to sample /samples supplied to this laboratory.
- 3- Sealed sample / Unsealed sample / Marked sample/Signed Samples
